



Southwest Quadrant Rehabilitation, City Project No. 20-002

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)

Funding Source		Expenses	
Federal Funds	\$ -	Project Budget	\$ 1,646,927.50
State Funds	\$ -	Total Expended	\$ 1,633,496.05
Measure L Funds	\$ 1,646,927.50		
Other	\$ -		
Total	\$ 1,646,927.50	Available	\$ 13,431.45

Project Details and Status:

City Council awarded the bid and approved an agreement in an amount of \$1,347,927.50 with George Reed, Inc. of Modesto, California, on June 13, 2023. The project includes different types of treatments on various roadways within the southwest quadrant of the City of Turlock. Construction is complete. Staff is working on Notice of Completion.

Completion Date: March 2024

Phase: Post Construction



Alaska Street



**Signal Coordination on W. Monte Vista Ave, Golden State Blvd, & Geer Rd,
City Project No. 20-038**

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)


Funding Source		Expenses	
Federal Funds	\$ 254,375.00	Project Budget	\$ 371,083.36
State Funds	\$ -	Total Expended	\$ 372,370.18
Measure L Funds	\$ 116,708.36		
Other	\$ -		
Total	\$ 371,083.36	Available	\$ (1,286.82)

Project Details and Status:

The project scope includes replacing the existing traffic signal controllers and installing new controllers that are capable of operating a signal timing plan. On August 9, 2022, City Council approved the contract with the low bidder, St. Francis Electric. The project is complete and the Notice of Completion was approved by City Council on June 25, 2024.

Completion Date: 6/25/24

Phase: Post Construction

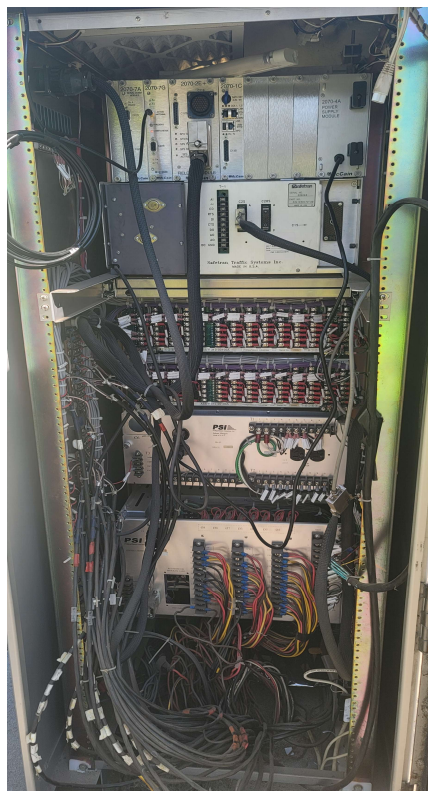

Control cabinet at Geer Rd and Hawkeye Ave with the new controller that was replaced.



Traffic Signal Synchronization on E. Monte Vista Avenue, City Project No. 20-039

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)


Funding Source		Expenses	
Federal Funds	\$ 70,088.74	Project Budget	\$ 86,783.18
State Funds	\$ -	Total Expended	\$ 91,019.21
Measure L Funds	\$ 16,694.44		
Other	\$ -		
Total	\$ 86,783.18	Available	\$ (4,236.03)

Project Details and Status:

The City of Turlock, in coordination with Caltrans, proposed to install a traffic signal synchronization timing plan to reduce vehicle stops and delays along E. Monte Vista Ave between Geer Rd. and Berkeley Ave. This involved replacing equipment with the existing controller boxes and installing new controllers that are capable of operating a signal timing plan. A signal coordination plan will help traffic signals operate more efficiently and reduce traffic congestion and improve local air quality. City Council approved Notice of Completion on June 25, 2024.

Completion Date: 6/25/24

Phase: Post Construction

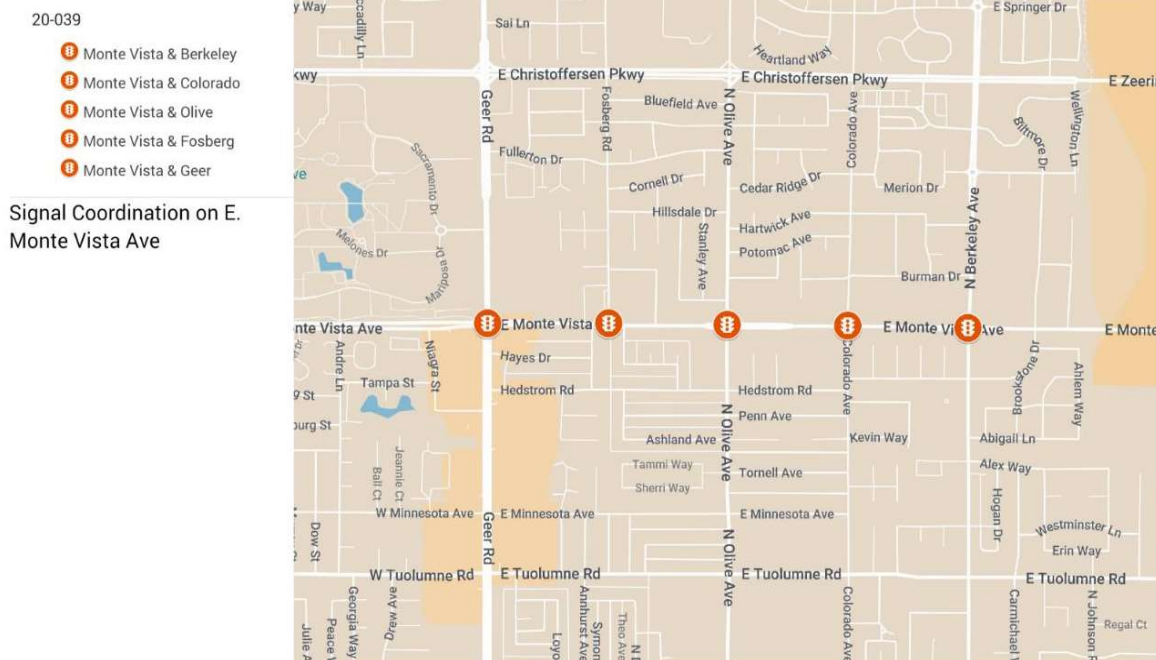



Pedras Road Rehabilitation, City Project No. 21-021

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)

Funding Source		Expenses	
Federal Funds	\$ 873,883.00	Project Budget	\$ 1,903,356.29
State Funds	\$ -	Total Expended	\$ 2,133,962.25
Measure L Funds	\$ 1,029,473.29		
Other	\$ -		
Total	\$ 1,903,356.29	Available	\$ (230,605.96)

Project Details and Status:

The project will rehabilitate aged pavement on Pedras Road between Geer Road and Golden State Boulevard. It will include construction of accessible pedestrian ramps, removing a valley gutter and installing storm drain improvements, and placement of new traffic striping. Construction commenced in April 2024. Concrete work has been completed, and the contractor will move to completing the road work.

Completion Date: August 2024

Phase: Construction





Traffic Signal Updates Various Locations, City Project No. 23-065

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)

Funding Source		Expenses	
Federal Funds	\$ -	Project Budget	\$ 3,000.00
State Funds	\$ -	Total Expended	\$ 2,746.59
Measure L Funds	\$ 3,000.00		
Other	\$ -		
Total	\$ 3,000.00	Available	\$ 253.41

Project Details and Status:

The project scope is to upgrade traffic signals at various locations that will include ADA push buttons, ADA countdown signal heads, and traffic signal head improvements.

Completion Date:

Phase: Pre Design



Washington Rd Bridge Railing Repair, City Project No. 22-005

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)

Funding Source		Expenses	
Federal Funds	\$ -	Project Budget	\$ 293,500.00
State Funds	\$ -	Total Expended	\$ 164,177.41
Measure L Funds	\$ 250,000.00		
SB 1 Funds	\$ 18,500.00		
Other (reimb)	\$ 25,000.00		
Total	\$ 293,500.00	Available	\$ 129,322.59

Project Details and Status:

The bridge railing on the east side of Washington Road crossing over TID Upper Lateral No. 4 was destroyed by a vehicular accident in 2020. The project scope includes the removal of existing damaged northbound bridge railing, repair of damaged concrete decking, and installation of anchor plates, posts, railing, and traffic energy dissipator end treatment. City Council awarded the contract to Bugler Construction Inc. on the October 11, 2022, City Council meeting. Construction started in January 2023. The project is complete and the Notice of Completion was approved on September 24, 2024.

Completion Date: 9/24/24

Phase: Ciomplete





Signal Coordination on Christoffersen Parkway, City Project No. 23-035 (CML 5165 (102))

Fiscal Year 2024-25, Quarter 1 (7/01/24 - 9/30/24)


Funding Source		Expenses	
Federal Funds	\$ 222,515.00	Project Budget	\$ 319,515.00
State Funds	\$ -	Total Expended	\$ 78,250.00
Measure L Funds	\$ 97,000.00		
Other	\$ -		
Total	\$ 319,515.00 Available		\$ 241,265.00

Project Details and Status:

The City of Turlock, in coordination with Caltrans, proposes to install a traffic signal synchronization timing plan to reduce vehicle stops and delays along Christoffersen Parkway. This involves replacing equipment with the existing controller boxes and installing new controllers that are capable of operating a signal timing plan. A signal coordination plan will help traffic signals operate more efficiently and reduce traffic congestion and improve local air quality.

Completion Date: TBD

Phase: Design

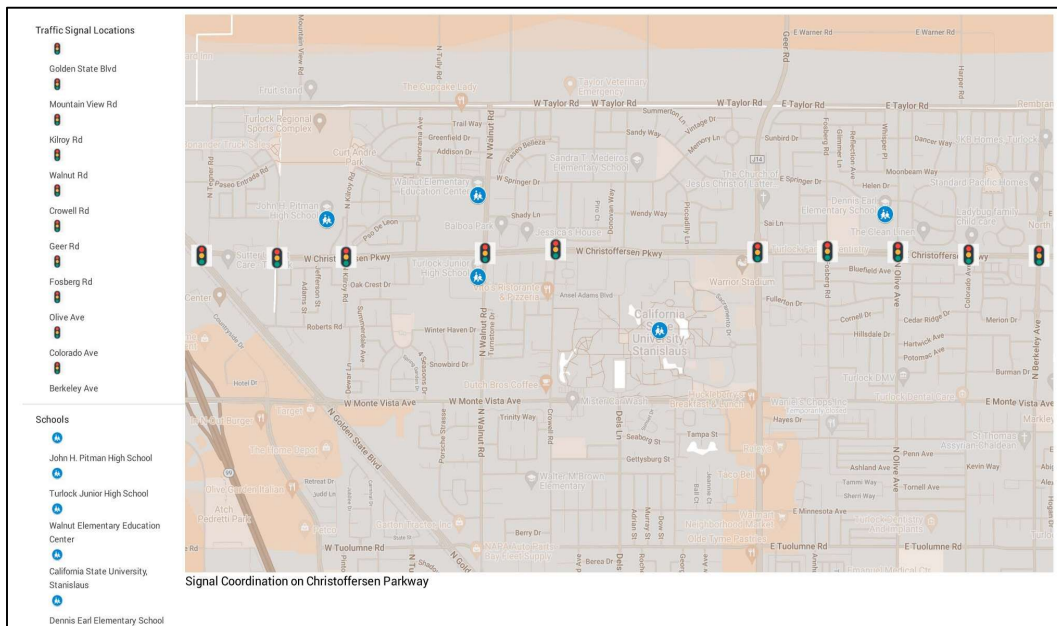

Project Area Map
